

STATE OF HAWAII
DEPARTMENT OF EDUCATION
KA 'OIHANA HO'ONA'AUAO
P.O. BOX 2360
HONOLULU, HAWAII 96804

OFFICE OF THE DEPUTY SUPERINTENDENT OF OPERATIONS

August 13, 2026

TO: The Honorable Ken Kuraya
Chairperson, Finance and Infrastructure Committee

FROM: Jesse Souki
Deputy Superintendent of Operations

A handwritten signature in blue ink, appearing to read "Jesse Souki", is placed to the right of the "FROM:" line.

SUBJECT: Department of Education update on status of schools' fire alarm systems

1. EXECUTIVE SUMMARY

This memorandum provides an update on the Hawaii State Department of Education's (Department) continued efforts to eliminate the need for manual fire watch plans by restoring and upgrading fire alarm systems, with a particular focus on recent successes.

The Department's progress is closely aligned with the Strategic Plan Goal 3.1.2, which ensures that the Department's school facility systems are responsive, efficient, and capable of addressing safety needs promptly.

2. DESCRIPTION

This update outlines the status of fire alarm system repairs, maintenance, and upgrades as part of the Department's ongoing fire safety improvement efforts. The completion of critical fire alarm projects, coupled with continued funding support for the design and construction of fire alarm system improvements, has significantly reduced the number of schools requiring fire watch.

3. UPDATE

Fire Alarm System Replacements


The Department continues to focus on ensuring fire alarm systems are replaced or repaired in a timely manner to enhance school safety as funding becomes available. As of July 22, 2026, the following updates are provided:

A. Fire Watch List

1. Five schools are currently on the fire watch list.
 - a. Hilo Intermediate School remains on fire watch. Fire alarms are operational but there is a disconnect back at the control board. Meanwhile, the design for the permanent upgrade was completed and the project was bid out and awarded. The project is pending permitting approvals and the contract execution is in progress. Construction duration is approximately 365 days.
 - b. Pahoa High and Intermediate School's system is operational, but does have intermittent issues with a portion of the underground wiring, so the school has decided to be on fire watch. The design for the permanent upgrade is completed and submitted for permitting. Funds are in the current fiscal year to be bid out.
 - c. Lanakila Elementary School remains on fire watch. Underground trouble shooting is required at Building D. The service contractor will commence testing and investigative work on August 17, 2026.
 - d. Aiea High School remains on fire watch. The service contractor will commence testing and investigation of the circuits and notification devices at Buildings A, E, and S by the first week of August 2026.
 - e. Waikele Elementary School remains on fire watch. The administration building and portables are down. The service contractor is awaiting parts to come in. Anticipated arrival is the end of July 2026 and work to be scheduled thereafter.
2. Completed. There are seven fire alarm replacement projects that have been completed in the last year:
 - a. Kalaniana'ole Elementary School
 - b. Lahainaluna High School
 - c. Pearl City High School
 - d. Heeia Elementary School
 - e. Nuuanu Elementary School
 - f. Kauluwela Elementary School
 - g. Fern Elementary School

3. Construction. There are currently 20 fire alarm replacement projects in various stages of construction:
 - a. Kapaa High School
 - b. Kainalu Elementary School
 - c. Hawaii School for the Deaf and Blind
 - d. Wilcox Elementary School
 - e. Waimea High School
 - f. Waipahu Intermediate School
 - g. Kaimuki High School
 - h. Kealakehe Intermediate School
 - i. August Ahrens Elementary School
 - j. Kohala Middle School
 - k. Jarrett Middle School
 - l. Ewa Elementary School
 - m. Ke Kula O Ehunuikaimalino
 - n. Leilehua High School
 - o. Sunset Beach Elementary School
 - p. Maemae Elementary School
 - q. Moanalua Middle School
 - r. Kapalama Elementary School
 - s. Kahuku High and Intermediate School
 - t. Laie Elementary School
4. Design. There are ten projects in design; determining what will be built, permitting, utility coordination, and preparing drawings for construction:
 - a. Konawaena Elementary School
 - b. Waianae Intermediate School
 - c. Kauai High School
 - d. Koloa Elementary School
 - e. Molokai High School
 - f. Pahoa High and Intermediate School
 - g. Lanai High and Intermediate School
 - h. Nanakuli High and Intermediate School
 - i. Kaneohe Elementary School
 - j. Puuhale Elementary School (24/7 monitoring only)
5. Scoped. There are seven projects being scoped to start design; identifying the issues and where improvements will go so that the scope of work can be determined for design to start:
 - a. Keaau High School
 - b. Keaau Middle School
 - c. Campbell High School
 - d. Kealakehe High School

- e. Pohakea Elementary School
- f. Waimea Elementary School
- g. Waikele Elementary School

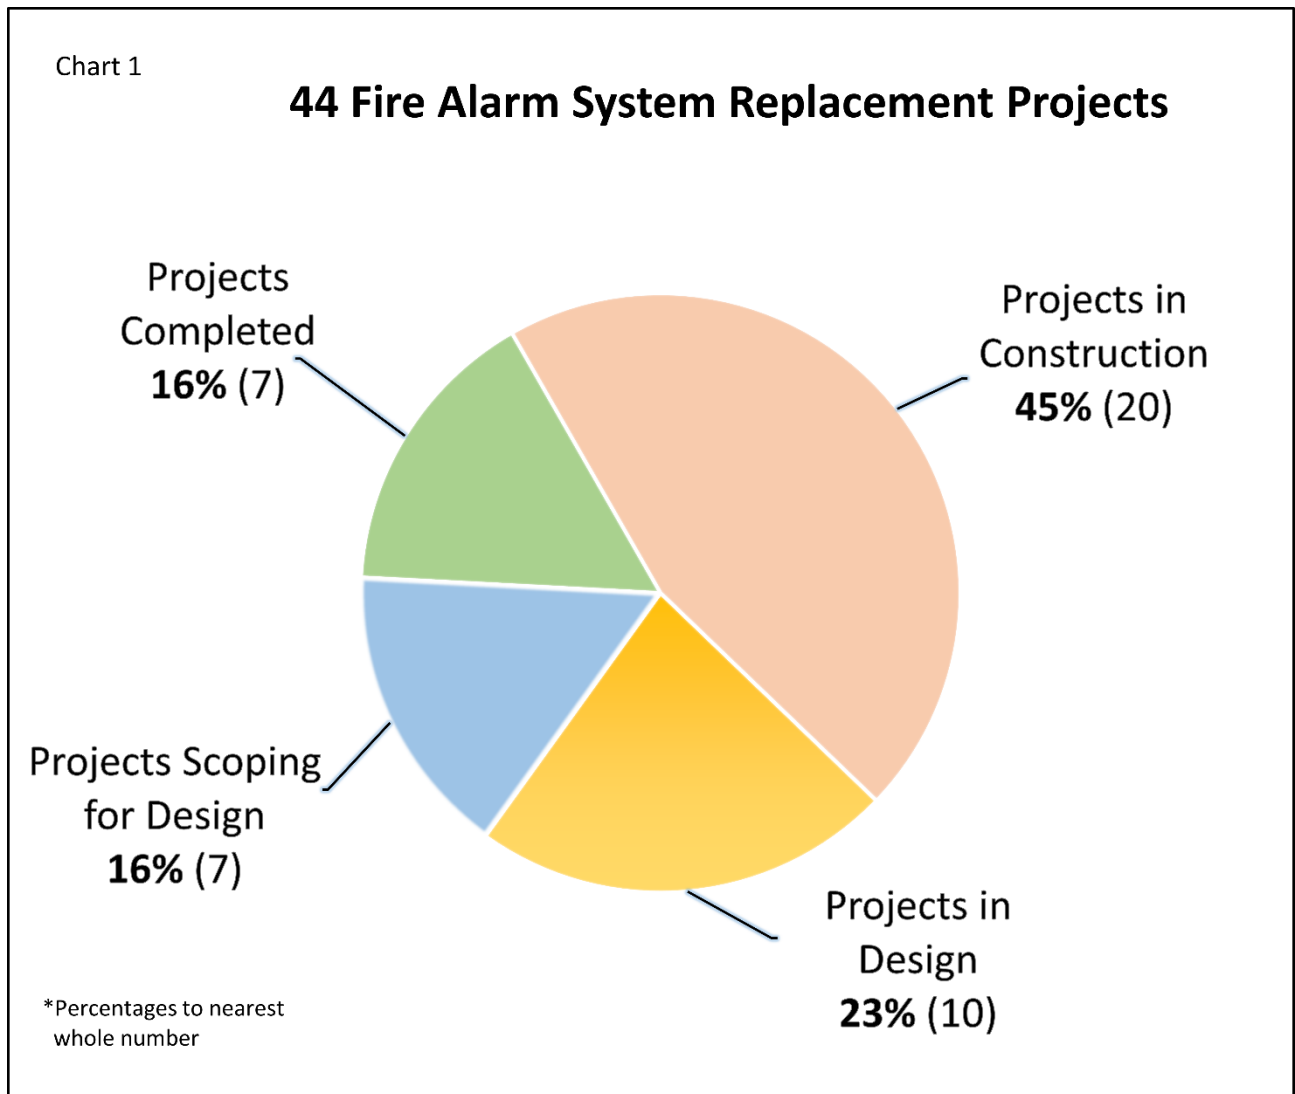


Inoperable Fire Alarm Mitigation Strategies

The Department continues to engage in the following:

- Exploring wireless fire alarm systems for rapid deployment in schools on fire watch. One wireless solution was successfully tested at Kapalama Elementary School before the Department fixed the school's fire alarm last school year.

- Collaborating with county fire departments to refine fire safety strategies and ensure compliance with regulatory requirements.
- Continuing to request for funding in the Department's Capital Improvement Program Health and Safety lump sum bucket. The Department appreciates the support of the Board, Legislature, and the Governor in providing an increase in funding this year in this bucket to allow the Department to fund more fire alarm upgrades.

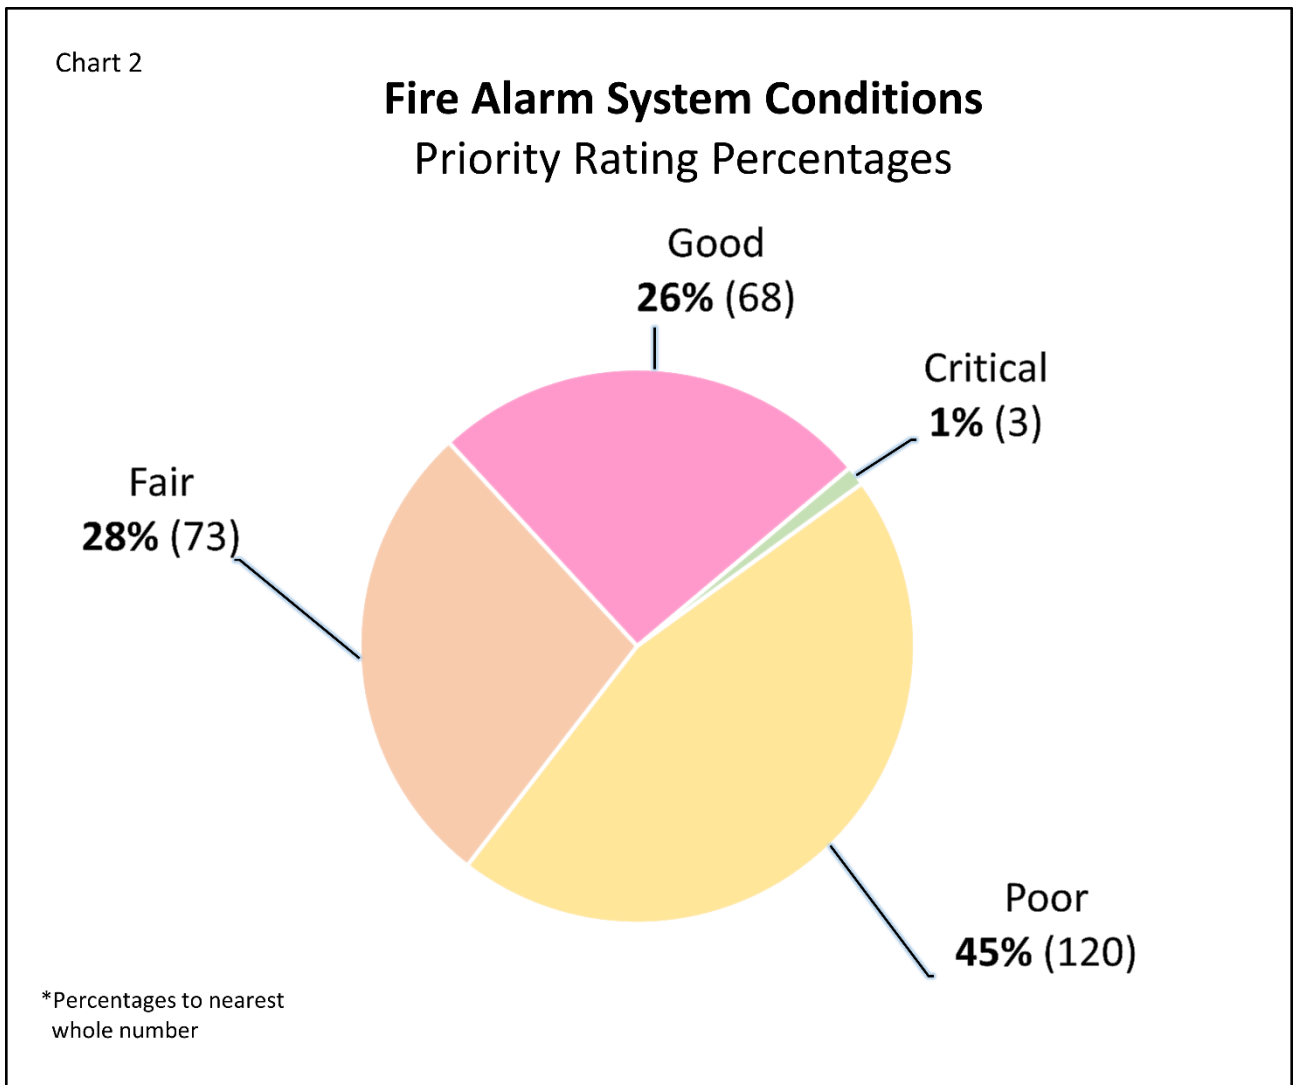

Legend

- Critical: System is non-functional or severely impaired requiring immediate action for full replacement.
Poor: System is functional but becoming unreliable due to age, recurring issues, or obsolete components.
Fair: System is functional and generally reliable but has identifiable deficiencies, aging components or maintenance needs that should be addressed as part of planned improvements.
Good: Fully operational and functional; routine maintenance only.

The Honorable Ken Kuraya
August 13, 2026
Page 6

The Department remains committed to prioritizing safety and continues to work towards ensuring all schools have fully operational fire alarm systems. The Department will maintain oversight of all school fire alarm systems, with priority given to those on the fire watch list, and will collaborate with state and county officials to fast-track funding and project approvals.

JS:ju
Attachment

c: Keith T. Hayashi, Superintendent
Heidi Armstrong, Deputy Superintendent of Academics
Tammi Oyadomari-Chun, Deputy Superintendent of Strategy and Administration
Amy Peckinpugh, Assistant Superintendent, Office of Information and
Technology Services
Sean Tajima, Assistant Superintendent, Office of Campus Operations and Support
Richard D. Fajardo, Assistant Superintendent, Office of Facilities and Operations
Facilities Development Branch

School Name	Priority	Score	Fire Watch	Age of FACP	Quantity of FACP's	Project Number	Last Milestone Date	Last Milestone	Cost Estimate	Construction Funded
HILO INTER	1	93%	Yes	23.5	3	P11243-24	6/26/2026	In Construction	\$1,931,295.00	Yes
WAIKELE ELEM	1	85%	Yes	12.5	6	-	-	Scoping	-	-
PAHOA HIGH & INTER	1	72%	Yes	29.33	2	P18304-23	4/26/2023	In Design	-	Yes
KONAWAENA ELEM	2	58%	-	26.5	3	P17210-23	12/26/2024	In Design	-	-
WAIANAE INTER	2	57%	-	29.08	1	P85212-22	12/13/2024	In Design	-	-
KAPAA HIGH	2	57%	-	25.25	1	P41211-22	5/18/2025	In Construction	\$2,730,747.00	Yes
KAPALAMA ELEM	2	57%	-	24	1	P21274-23	3/25/2026	In Construction	\$1,298,869.00	Yes
CAMPBELL HIGH	2	56%	-	24.5	8	P81552-25	-	Scoping	-	-
KEALAKEHE HIGH	2	55%	-	30.08	5	P15560-26	-	Scoping	-	-
KAINALU ELEM	2	53%	-	41.08	1	P94004-10	6/1/2025	In Construction	\$ 247,500.00	Yes
POHAKEA ELEM	2	53%	-	35.08	1	P81553-25	-	Scoping	-	-
KAUAI HIGH	2	53%	-	31.08	2	P42227-23	1/1/2025	In Design	-	-
KEAUKAHA ELEM	2	53%	-	31.08	1	-	-	-	-	-
WAIKAE ELEM	2	53%	-	31.08	1	P12561-26	-	Scoping	-	-
MAUKA LANI ELEM	2	53%	-	30.08	1	-	-	-	-	-
KAU HIGH & PAHALA ELEM	2	53%	-	29.08	1	-	-	-	-	-
MAUI HIGH	2	53%	-	29.08	1	-	-	-	-	-
STEVENSON MIDDLE	2	53%	-	28.83	1	12-16-0297 (DAGS)	4/1/1996	Completed	-	Yes
WASHINGTON MIDDLE	2	53%	-	27.75	1	-	-	-	-	-
WHEELER ELEM	2	53%	-	26.5	1	-	-	-	-	-
KONAWAENA MIDDLE	2	53%	-	26.08	2	-	-	-	-	-
HAWAII SCHOOL FOR DEAF & BLIND (SCSHVI)	2	53%	-	26.08	1	P25272-23	6/17/2025	In Construction	\$1,342,650.00	Yes
WAIMALU ELEM	2	53%	-	25.5	1	57-16-2178 (DAGS)	9/7/1999	Completed	-	Yes
MAKAWAO ELEM	2	53%	-	24.08	1	-	-	-	-	-
KEAAU HIGH	2	53%	-	23.58	1	Q14246-20	2/3/2022	Scoping	-	-
MOANALUA HIGH	2	53%	-	23.5	2	-	-	-	-	-
NAALEHU ELEM	2	53%	-	23.5	1	51-16-3306 (DAGS)	7/30/2001	Completed	-	Yes
WAIANAE HIGH	2	53%	-	23.08	3	-	-	-	-	-
WAIKOLOA ELEM & MIDDLE	2	53%	-	21.5	2	-	-	-	-	-
KIPAPA ELEM	2	53%	-	20.08	1	57-16-4508 (DAGS)	11/18/2005	Completed	-	Yes
HICKAM ELEM	2	53%	-	17.5	1	P00955-06	1/18/2008	Completed	-	Yes
PUUNENE	2	48%	-	5.67	1	-	-	-	-	-
MOMILANI ELEM	2	47%	-	12.17	3	P84005-07	5/20/2014	Completed Within 15 Years	-	-
WAIKAE MIDDLE PCCS	2	47%	-	32.5	2	-	-	-	-	-
WAIPAHU ELEM	2	47%	-	24.33	2	58-16-3700 (DAGS)	11/6/2003	Completed	-	Yes
AIEA HIGH	2	43%	Yes	8.5	2	P71002-11	5/29/2014	Completed Within 15 Years	-	-
WILCOX ELEM	2	40%	-	46.08	1	P42226-23	5/9/2025	In Construction	\$1,643,000.00	Yes
LEIHOKU ELEM	2	40%	-	36.5	2	-	-	-	-	-
KOLOA ELEM	2	40%	-	35.08	1	P42228-23	12/26/2024	In Design	-	-
KALANIANA'OLE ELEM & INTER	2	40%	-	32	1	P11000-17	6/1/2023	Completed	\$ 769,525.00	Yes
WAIKAE HIGH	2	40%	-	31.75	3	P43225-23	6/23/2025	In Construction	\$3,343,440.00	Yes
WAIPAHU INTER	2	40%	-	31.58	1	P86005-13	4/24/2022	In Construction	\$2,212,943.00	-
ALIOLANI ELEM	2	40%	-	31.33	1	-	-	-	-	-
KAIMUKI HIGH	2	40%	-	31.17	5	P24201-22	10/9/2023	In Construction	\$3,500,000.00	Yes
JEFFERSON ELEM	2	40%	-	31.08	1	-	-	-	-	-
KAHUKU ELEM	2	40%	-	30.92	1	P92003-14	-	-	-	-
WAIKAEWAENA ELEM	2	40%	-	30.58	1	31-16-7458 (DAGS)	12/4/1995	Completed	-	Yes
KAMALII ELEM	2	40%	-	30.5	1	-	-	-	-	-
IAO INTER	2	40%	-	30.08	1	-	-	-	-	-
MILILANI UKA ELEM	2	40%	-	30.08	1	12-16-4211 (DAGS)	5/29/1996	Completed	-	Yes

Department of Education Fire Alarm Priority List
July 2026

Attachment

HANALEI ELEM	2	40%	-	29.92	1	-	-	-	-	-
HOOKENA ELEM	2	40%	-	29.08	1	-	-	-	-	-
LAUPAHOEHOE COMMUNITY PCS	2	40%	-	29.08	1	-	-	-	-	-
MOANALUA MIDDLE	2	40%	-	29.08	1	P74001-17	11/1/2022	In Construction	-	Yes
KONAWAENA HIGH	2	40%	-	29	4	-	-	-	-	-
MOLOKAI MIDDLE (SHARES SYSTEM WITH HS)	2	40%	-	28.5	-	-	-	-	-	-
MOLOKAI HIGH	2	40%	-	28.5	1	P57011-10	1/6/2017	In Design	-	-
PAHOA ELEM	2	40%	-	28.5	1	-	-	-	-	-
KAPOLEI MIDDLE	2	40%	-	27.5	3	-	-	-	-	-
DE SILVA ELEM	2	40%	-	27.5	1	-	-	-	-	-
KAMAKAHELEI MIDDLE	2	40%	-	27.08	6	-	-	-	-	-
KAPOLEI HIGH	2	40%	-	26.5	9	-	-	-	-	-
HOLUALOA ELEM	2	40%	-	26.5	1	-	-	-	-	-
KAUMANA ELEM	2	40%	-	26.5	1	51-16-1955 (DAGS)	12/15/1998	Completed	-	Yes
WAIKEA HIGH	2	40%	-	26.5	1	-	-	-	-	-
MAILI ELEM	2	40%	-	26.33	1	58-16-1978 (DAGS)	3/20/2000	Completed	-	Yes
PAUOA ELEM	2	40%	-	26.25	1	-	-	-	-	-
KULA ELEM	2	40%	-	26.08	2	-	-	-	-	-
HAIKU ELEM	2	40%	-	26.08	1	15-16-2549 (DAGS)	5/1/2000	Completed	-	Yes
KAILUA ELEM	2	40%	-	26.08	1	59-16-1861 (DAGS)	Jan-99	Completed	-	Yes
KAWANANAKOA MIDDLE	2	40%	-	26.08	1	-	-	-	-	-
KUALAPUU PCCS	2	40%	-	26.08	1	55-16-1827 (DAGS)	10/1/1998	Completed	-	Yes
ALVAH SCOTT ELEM	2	40%	-	25.75	1	12-16-2546 (DAGS)	10/4/2000	Completed	-	Yes
KEAAU MIDDLE	2	40%	-	25.5	4	-	-	Scoping	-	-
PEARL RIDGE ELEM	2	40%	-	25.5	1	-	-	-	-	-
HAUULA ELEM	2	40%	-	25.08	1	-	-	-	-	-
IROQUOIS POINT ELEM	2	40%	-	25.08	1	-	-	-	-	-
ANUENUE SCHOOL	2	40%	-	24.92	1	52-16-3591(C) (DAGS)	10/1/2026	Completed	-	Yes
WILSON ELEM	2	40%	-	24.75	1	-	-	-	-	-
HILO UNION ELEM	2	40%	-	24.5	1	-	-	-	-	-
PEARL CITY HIGHLANDS ELEM	2	40%	-	24.5	1	58-16-4166 (DAGS)	3-Feb	Completed	-	Yes
KOHALA ELEM (FA SYSTEM ON HS)	2	40%	-	24.08	-	-	-	-	-	-
KAAHUMANU ELEM	2	40%	-	24.08	1	-	-	-	-	-
KAELEPULU ELEM	2	40%	-	24.08	1	59-16-3376 (DAGS)	8/1/2026	Completed	-	Yes
KALANI HIGH	2	40%	-	24.08	1	12-16-2543 (DAGS)	1-Mar	Completed	-	Yes
MAUNALOA ELEM	2	40%	-	24.08	1	-	-	-	-	-
HONAUNAU ELEM	2	40%	-	23.92	1	-	-	-	-	-
KAHAKAI ELEM	2	40%	-	23.92	1	51-16-3261 (DAGS)	8/1/2002	Completed	-	Yes
KEALAKEHE INTER	2	40%	-	23.5	1	P15208-23	6/9/2025	In Construction	\$1,595,378.00	Yes
KEALAKEHE ELEM	2	40%	-	23.5	1	-	-	-	-	-
KALIHI KAI ELEM	2	40%	-	23.5	1	-	-	-	-	-
MAEMAE ELEM	2	40%	-	23.5	1	P22000-18	7/18/2025	In Construction	\$1,236,656.00	Yes
PAAUILO ELEM & INTER	2	40%	-	23.5	1	-	-	-	-	-
PALOLO ELEM	2	40%	-	23.5	1	-	-	-	-	-
RED HILL ELEM	2	40%	-	23.5	1	57-16-3575 (DAGS)	5/1/2026	Completed	-	Yes
WAIKEA ELEM	2	40%	-	23.5	1	-	-	-	-	-
KAILUA INTER	2	40%	-	23.42	1	59-16-3739 (DAGS)	1/24/2003	Completed	-	Yes
AUGUST AHRENS ELEM	2	40%	-	23.08	1	P86215-23	6/30/2025	In Construction	\$1,488,345.00	Yes
KEKAHA ELEM	2	40%	-	23.08	1	59-16-4338 (DAGS)	3/23/2005	Completed	-	Yes
KOHALA MIDDLE	2	40%	-	23.08	1	P16209-23	6/17/2025	In Construction	\$1,023,990.00	Yes
JARRETT MIDDLE	2	40%	-	22.5	1	P24273-23	1/31/2025	In Construction	\$1,118,515.00	Yes
HIGHLANDS INTER	2	40%	-	22.42	1	-	-	-	-	-

Department of Education Fire Alarm Priority List
July 2026

Attachment

WAHIAWA ELEM	2	40%	-	22.08	2	57-16-5193, 57-16-4155	9/19/2003	Completed	-	Yes
PEARL HARBOR ELEM	2	40%	-	21.92	1	57-16-5194 (DAGS)	8/29/2003	Completed	-	Yes
PEARL HARBOR KAI ELEM	2	40%	-	21.83	1	-	-	-	-	-
WAIALUA ELEM	2	40%	-	21.75	1	-	-	-	-	-
MILILANI WAENA ELEM	2	40%	-	21.5	1	57-16-5186 (DAGS)	9/3/2003	Completed	-	Yes
KALEIOPUU ELEM	2	40%	-	21.25	2	58-16-3675 (DAGS)	4/6/2005	Completed	-	Yes
HAHAIONE ELEM	2	40%	-	21.25	1	12-16-2543 (DAGS)	3/28/2005	Completed	-	Yes
MAUNAWILI ELEM	2	40%	-	21.08	1	59-16-4199 (DAGS)	3/10/2004	Completed	-	Yes
HELEMANO ELEM	2	40%	-	21.08	1	57-16-4506 (DAGS)	2/13/2004	Completed	-	-
EWA BEACH ELEM	2	40%	-	20.67	1	-	-	-	-	-
PEARL CITY ELEM	2	40%	-	20.5	1	58-16-5759 (DAGS)	9-Aug	Completed	-	Yes
KAIMILOA ELEM	2	40%	-	20.17	1	-	-	-	-	-
KILOHANA ELEM	2	40%	-	20.08	1	55-16-5778 (DAGS)	8/5/2026	Completed	-	Yes
KAUNAKAKAI ELEM	2	40%	-	19.25	1	55-16-5778 (DAGS)	8/1/2005	Completed	-	Yes
AHUIMANU ELEM	2	40%	-	18.92	1	-	-	-	-	-
EWA ELEM	2	40%	-	18.67	1	P81216-23	7/17/2025	In Construction	\$1,594,058.00	Yes
HANA HIGH & ELEM	2	40%	-	18	1	-	-	-	-	-
PALISADES ELEM	2	40%	-	17.75	1	-	-	-	-	-
LEHUA ELEM	2	40%	-	17.75	1	-	-	-	-	-
HONOKAA HIGH & INTER	2	40%	-	16.67	1	51-16-3260 (DAGS)	4/1/2008	Completed	-	Yes
LINAPUNI ELEM	2	40%	-	16.42	1	-	-	-	-	-
WAILUKU ELEM	3	40%	-	14.75	1	P100116-2	9/5/2013	Completed Within 15 Years	-	Yes
POMAIKAI ELEM	3	39%	-	4.25	1	P55278-21	3/23/2022	Completed Within 15 Years	\$ 98,661.29	Yes
KEAAU ELEM	3	39%	-	4.08	1	-	-	-	-	-
ROYAL ELEM	3	39%	-	14	1	P01052-06	7/1/2012	Completed Within 15 Years	-	-
LANAKILA ELEM	3	38%	Yes	15.42	1	P01229-06	7/27/2011	Completed Within 15 Years	-	-
MCKINLEY HIGH	3	37%	-	36.5	7	12-16-1021 (DAGS)	1/1/1990	Completed	-	Yes
HILO HIGH	3	37%	-	24.5	3	-	-	-	-	-
HONOKAA ELEM	3	36%	-	12.08	1	51-16-3260 (DAGS)	4/1/2008	Completed	-	Yes
PUUHALE ELEM	3	36%	-	12.08	1	P21018-07	5/14/2014	Design for 24/7 monitoring	\$ 129,664.00	Yes
KE KULA O EHUNUIKAIMALINO	3	36%	-	12	1	P17006-07	7/10/2024	In Construction	\$ 455,526.00	Yes
LAIE ELEM	3	36%	-	1.75	1	P92001-18	10/8/2024	In Construction	\$ 540,575.00	Yes
NOELANI ELEM	3	36%	-	21.83	3	-	-	-	-	-
ROOSEVELT HIGH	3	35%	-	18.5	2	-	-	-	-	-
HALEIWA ELEM	3	34%	-	10.33	1	P76801-08	8/2/2016	Completed Within 15 Years	-	Yes
KANEOHE ELEM	3	33%	-	25.08	2	12-16-2547 (DAGS)	4/1/2000	In Design	-	Yes
AIEA ELEM	3	33%	-	24.33	1	57-16-3540 (DAGS)	2/22/2002	Completed	-	Yes
POPE ELEM	3	33%	-	23.5	1	59-16-3381 (DAGS)	5/28/2004	Completed	-	Yes
ALA WAI ELEM	3	33%	-	23.08	1	52-16-4086 (DAGS)	12/1/2003	Completed	-	Yes
ALIAMANU MIDDLE	3	33%	-	23.08	1	57-16-5143 (DAGS)	2/20/2003	Completed	-	Yes
PUOHALA ELEM	3	33%	-	22.5	1	59-16-3757 (DAGS)	9/12/2002	Completed	-	Yes
WAHIAWA MIDDLE	3	33%	-	22.5	1	-	-	-	-	-
BARBERS POINT ELEM	3	33%	-	22.5	1	-	-	-	-	-
FARRINGTON HIGH	3	33%	-	22.33	3	-	-	-	-	-
KEOLU ELEM	3	33%	-	22.33	1	59-16-4192 (DAGS)	3/12/2004	Completed	-	Yes
NANAIKAPONO ELEM	3	33%	-	22.08	3	-	-	-	-	-
KAHALA ELEM	3	33%	-	22	1	-	-	-	-	-
HOKULANI ELEM	3	33%	-	21.83	1	-	-	-	-	-
NANAKULI HIGH & INTER	3	33%	-	21.5	1	-	-	In Design	-	-
ILIMA INTER	3	33%	-	21.5	1	-	-	-	-	-
MILILANI IKE ELEM	3	33%	-	21.08	1	12-16-3960 (DAGS)	Jun-02	Completed	-	Yes
KEONEULA ELEM	3	33%	-	20.5	1	-	-	-	-	-

Department of Education Fire Alarm Priority List
July 2026

Attachment

MANOA ELEM	3	33%	-	20.33	1	-	-	-	-	-
KAISER HIGH	3	33%	-	19.33	4	52-16-4520 (DAGS)	8/4/2026	Completed	-	Yes
LUNALILO ELEM	3	33%	-	18.83	1	-	-	-	-	-
INOUE ELEM	3	33%	-	18.58	1	P00959-06	4/10/2008	Completed	-	Yes
RADFORD HIGH	3	33%	-	18.5	5	-	-	-	-	-
SALT LAKE ELEM	3	33%	-	18.5	1	-	-	-	-	-
NANAKULI ELEM	3	33%	-	18.5	1	-	-	-	-	-
LIHOLIHO ELEM	3	33%	-	18.42	1	-	-	-	-	-
LEILEHUA HIGH	3	33%	-	18.33	1	P72007-19	7/1/2025	In Construction	-	Yes
ALIAMANU ELEM	3	33%	-	18.33	1	P00954-06	3/14/2008	Completed	-	Yes
MAKAKILO ELEM	3	33%	-	17.83	1	-	-	-	-	-
MAKALAPA ELEM	3	33%	-	17.67	1	P00935-06	11/5/2008	Completed	-	Yes
LINCOLN ELEM	3	33%	-	17.5	1	-	-	-	-	-
KAIULANI ELEM	3	33%	-	17.17	1	-	-	-	-	-
SHAFTER ELEM	3	33%	-	17	1	-	-	-	-	-
KEELIKOLANI MIDDLE	3	33%	-	16.83	1	-	-	-	-	-
MOKAPU ELEM	3	33%	-	16.75	1	P94035-07	6/1/2009	Completed	-	Yes
KAMAILE ACADEMY PCS	3	33%	-	16.25	1	P85001-07/P85002-07	4/10/2026	Completed Within 15 Years	-	Yes
KAALA ELEM	3	33%	-	15.83	1	P00653-06	9/21/2010	Completed Within 15 Years	-	Yes
WAIHEE ELEM	3	33%	-	9.92	1	-	-	-	-	-
WEBLING ELEM	3	32%	-	8.92	1	-	-	-	-	-
WAIPAHU HIGH	3	32%	-	32.08	3	-	-	-	-	-
EWA MAKAI MIDDLE	3	31%	-	15.75	2	Q81002-07	10/18/2010	Completed Within 15 Years	-	-
KOHALA HIGH	3	30%	-	24.08	1	-	-	-	-	-
KALIHI ELEM	3	30%	-	12.17	1	-	-	-	-	-
PARKER ELEM	3	29%	-	6.83	2	P91801-08	1/2/2020	Completed Within 15 Years	\$ 526,900.00	Yes
WAIHAOLE ELEM	3	28%	-	11.33	1	P91003-13	Oct-15	Completed Within 15 Years	-	Yes
WHEELER MIDDLE	3	28%	-	11.17	1	-	-	-	-	-
AIKAHI ELEM	3	28%	-	11.08	1	57-16-4180 (DAGS)	11/2/2026	Completed	-	Yes
DOLE MIDDLE	3	28%	-	6.08	2	P21002-07	Jun-20	Completed Within 15 Years	\$ 837,063.00	Yes
WAIANAE ELEM	3	27%	-	5.25	1	Q85000-14	11/7/2019	Completed Within 15 Years	\$6,819,870.23	Yes
LIKELIKE ELEM	3	27%	-	10.08	1	-	-	-	-	-
KAILUA HIGH	3	27%	-	24.08	3	59-16-3379 (DAGS)	3/1/2026	Completed	-	Yes
HONOWAI ELEM	3	27%	-	21.75	2	58-16-5748 (DAGS)	9/29/2004	Completed	-	Yes
NIU VALLEY MIDDLE	3	27%	-	16.42	2	P26008-07	10/12/2010	Completed Within 15 Years	-	Yes
KOKO HEAD ELEM	3	24%	-	8.17	10	P26004-13	4/25/2018	Completed Within 15 Years	-	Yes
AIEA INTER	3	23%	-	7.58	2	P71805-08	11/28/2018	Completed Within 15 Years	\$ 660,834.00	Yes
MOKULELE ELEM	3	22%	-	6.67	3	P75018-10	5/22/2019	Completed Within 15 Years	-	Yes
HONOULIULI MIDDLE	3	21%	-	5.83	6	-	-	-	-	-
LIHIKAI ELEM	3	21%	-	5.83	1	-	-	-	-	-
MOUNTAIN VIEW ELEM	3	20%	-	12	3	-	-	-	-	-
ELEELE ELEM	3	20%	-	15.5	1	-	-	-	-	-
KAPIOLANI ELEM	4	19%	-	13.92	3	-	-	-	-	-
KAPOLEI ELEM	4	19%	-	13.92	2	-	-	-	-	-
KALIHI WAENA ELEM	4	18%	-	13.83	5	-	-	-	-	-
MANANA ELEM	4	18%	-	13.58	1	-	-	-	-	-
PUU KUKUI ELEM	4	17%	-	13.08	7	-	-	-	-	-
KIHEI ELEM	4	17%	-	13.08	1	P55014-10	-	Completed	-	-
KALAHEO ELEM	4	17%	-	12.92	2	P94006-14	7/29/2020	Completed Within 15 Years	\$1,116,817.15	Yes
WAIKIKI ELEM	4	17%	-	12.75	1	P25803-08	2/11/2026	Completed Within 15 Years	-	-
PUKALANI ELEM	4	17%	-	12.67	1	P53808-08	12-May	Completed Within 15 Years	-	-
MILILANI MIDDLE	4	17%	-	12.5	9	-	-	-	-	-

Department of Education Fire Alarm Priority List
July 2026

Attachment

KAHULUI ELEM	4	16%	-	11.75	1	P55001-10	13-Mar	Completed Within 15 Years	-	-
PAIA ELEM	4	15%	-	11.5	2	-	-	-	-	-
BALDWIN HIGH	4	15%	-	11.33	2	P51001-10	8/10/2015	Completed Within 15 Years	-	Yes
HOOKELE ELEM	4	15%	-	11.08	1	-	-	-	-	-
LOKELANI INTER	4	14%	-	10.75	1	55-16-5786 (DAGS)	3/31/2004	Completed	-	Yes
WAIU ELEM	4	14%	-	10.75	1	-	-	-	-	-
LANAI HIGH & ELEM	4	14%	-	10.58	3	Q56329-24	4/10/2025	In Design	\$2,325,820.00	-
LAHAINA INTER	4	14%	-	5.25	2	P54006-10	4/20/2021	Completed Within 15 Years	\$ 392,634.00	Yes
MAKAHA ELEM	4	13%	-	10.08	1	-	-	-	-	-
KANOELANI ELEM	4	13%	-	9.92	2	-	-	-	-	-
NIMITZ ELEM	4	13%	-	9.83	4	P75005-07	12/5/2016	Completed Within 15 Years	-	-
ENCHANTED LAKE ELEM	4	12%	-	9.08	1	-	-	-	-	-
WAIMANALO ELEM & INTER	4	12%	-	9	1	32-16-4553 (DAGS)	12/24/1993	Completed	-	Yes
WAIALAE ELEM PCS	4	12%	-	8.92	4	P25024-10	7/26/2017	Completed Within 15 Years	\$ 489,017.23	Yes
MOANALUA ELEM	4	11%	-	8.33	2	P74801-08	3/20/2018	Completed Within 15 Years	-	Yes
WAIALUA HIGH & INTER	4	11%	-	7.92	24	P00658-06	7/27/2018	Completed Within 15 Years	\$1,157,126.00	Yes
MILILANI MAUKA ELEM	4	11%	-	7.92	4	P73004-11	8/8/2018	Completed Within 15 Years	\$ 627,413.39	Yes
KING INTER	4	10%	-	7.75	1	P91010-07	10/11/2018	Completed Within 15 Years	\$ 902,859.76	Yes
CASTLE HIGH	4	10%	-	7.58	17	P91001-07	5/7/2012	Completed Within 15 Years	-	Yes
WAHIAWA STOREFRONT	4	10%	-	7.5	1	-	-	-	-	-
SOLOMON ELEM	4	9%	-	7.08	3	Q72003-13	2/11/2021	Completed Within 15 Years	-	-
MILILANI HIGH	4	9%	-	7	17	P73804-08	7/16/2019	Completed Within 15 Years	\$1,151,149.00	Yes
WAIAKEA INTER	4	8%	-	6.33	1	P19003-11	3/20/2020	Completed Within 15 Years	\$ 556,617.00	Yes
KALAEHO HIGH	4	8%	-	5.92	13	P94006-14	7/29/2020	Completed Within 15 Years	\$1,116,817.15	Yes
KAPAA ELEM	4	8%	-	5.92	6	P41000-16	3/3/2021	Completed Within 15 Years	\$ 910,343.16	Yes
KULANIHAKOI HIGH	4	8%	-	5.67	4	-	-	-	-	-
ILIAHI ELEM	4	7%	-	5.5	7	P72001-11	10/20/2020	Completed Within 15 Years	\$ 944,675.00	Yes
WAIMEA CANYON MIDDLE	4	7%	-	5.5	2	-	-	-	-	-
AINA HAINA ELEM	4	7%	-	5.33	1	P26001-10	3/19/2021	Completed Within 15 Years	\$ 724,756.64	Yes
NAHIENAENA ELEM	4	7%	-	5.25	2	P54001-17	4/14/2021	Completed Within 15 Years	\$ 379,272.00	Yes
KAAWA ELEM	4	7%	-	5.17	1	P92001-16	7/7/2021	Completed Within 15 Years	\$ 294,688.00	Yes
MAUI WAENA INTER	4	7%	-	5.17	1	P55005-13	2/12/2021	Completed Within 15 Years	\$ 859,779.47	Yes
KILAEUA ELEM	4	7%	-	5.08	7	P41001-14	5/26/2021	Completed Within 15 Years	\$ 428,828.00	Yes
KALAMA INTER	4	7%	-	5.08	3	P53001-16	2/16/2023	Completed Within 15 Years	\$ 678,410.00	Yes
KALAKAUA MIDDLE	4	7%	-	5	11	P21807-08	5/19/2021	Completed Within 15 Years	\$ 962,820.79	Yes
KALIHI UKA ELEM	4	7%	-	5	3	P21006-13	7/1/2021	Completed Within 15 Years	\$ 254,442.78	Yes
HOLOMUA ELEM	4	6%	-	4.67	4	P81003-17	10/6/2021	Completed Within 15 Years	\$ 728,646.00	Yes
KAPAA MIDDLE	4	6%	-	4.25	11	P41016-10	4/19/2022	Completed Within 15 Years	\$1,039,410.26	Yes
HAAHEO ELEM	4	6%	-	4.25	1	P11003-11	3/16/2021	Completed Within 15 Years	\$ 227,515.00	Yes
KAMILOKI ELEM	4	5%	-	3.92	5	P26018-10	12/22/2022	Completed Within 15 Years	\$ 561,941.00	Yes
KAUWAI ELEM	4	5%	-	3.5	6	P21002-16	1/10/2023	Completed Within 15 Years	\$ 464,157.68	Yes
KAPUNAHALA ELEM	4	4%	-	3	1	P91000-18	12/5/2022	Completed Within 15 Years	\$ 366,049.00	Yes
KAIMUKI MIDDLE	4	4%	-	2.92	9	P24804-08	1/31/2024	Completed Within 15 Years	\$ 903,441.86	Yes
KEONEPOKO ELEM	4	4%	-	2.83	7	P18000-18	9/8/2023	Completed Within 15 Years	\$ 766,110.00	Yes
KAHALUU ELEM	4	3%	-	2.58	5	Q91214-19	4/3/2025	Punchlist	\$ 463,072.00	Yes
OLOMANA SCHOOL	4	3%	-	2.58	1	P69212-19	8/2/2024	Completed Within 15 Years	\$1,545,254.50	Yes
KAHAAO ELEM PCS	4	3%	-	2.5	4	Q94000-15	5/9/2023	Completed	-	-
KEKAULIKE HIGH	4	3%	-	2.49	19	P53004-16	9/20/2023	Completed Within 15 Years	\$1,441,633.00	Yes
FERN ELEM	4	3%	-	2.17	6	Q21228-19	6/27/2024	Completed	\$ 499,302.00	Yes
NUUANU ELEM	4	3%	-	2.17	2	P01054-06	3/27/2024	Completed	\$ 354,716.00	Yes
KAUMUALII ELEM	4	3%	-	2.08	8	P42215-22	7/29/2024	Completed Within 15 Years	\$1,189,190.00	Yes
KUHIO ELEM	4	3%	-	2	6	P24223-20	5/28/2024	Completed Within 15 Years	\$ 412,041.00	Yes

Department of Education Fire Alarm Priority List
July 2026

Attachment

HEEIA ELEM	4	3%	-	1.92	7	P91003-14	8/14/2024	Completed	\$ 675,000.00	Yes
PEARL CITY HIGH	4	2%	-	1.42	15	P84200-22	1/21/2025	Completed	\$1,924,378.00	Yes
LAHAINALUNA HIGH	4	2%	-	1.33	21	P54200-22	3/1/2025	Completed	\$3,282,110.00	Yes
KAHUKU HIGH & INTER	4	2%	-	1.33	1	P92220-21	3/28/2025	In Construction	\$1,040,522.00	Yes
SUNSET BEACH ELEM	4	2%	-	1.25	2	P92802-08	1/4/2025	In Construction	\$ 902,842.00	Yes
KAULUWELA ELEM	4	1%	-	0.5	6	P23000-15	2/14/2025	Completed	\$ 447,515.00	Yes
KAMEHAMEHA III ELEM	9	INC	-		-	-	-	-	-	-
NIIHAU SCHOOL	9	INC	-		-	-	-	-	-	-
